






Council of State & Territorial Epidemiologist
2635 Century Parkway, N.E.; Suite 700
Atlanta, Georgia 30345
Project Schedule

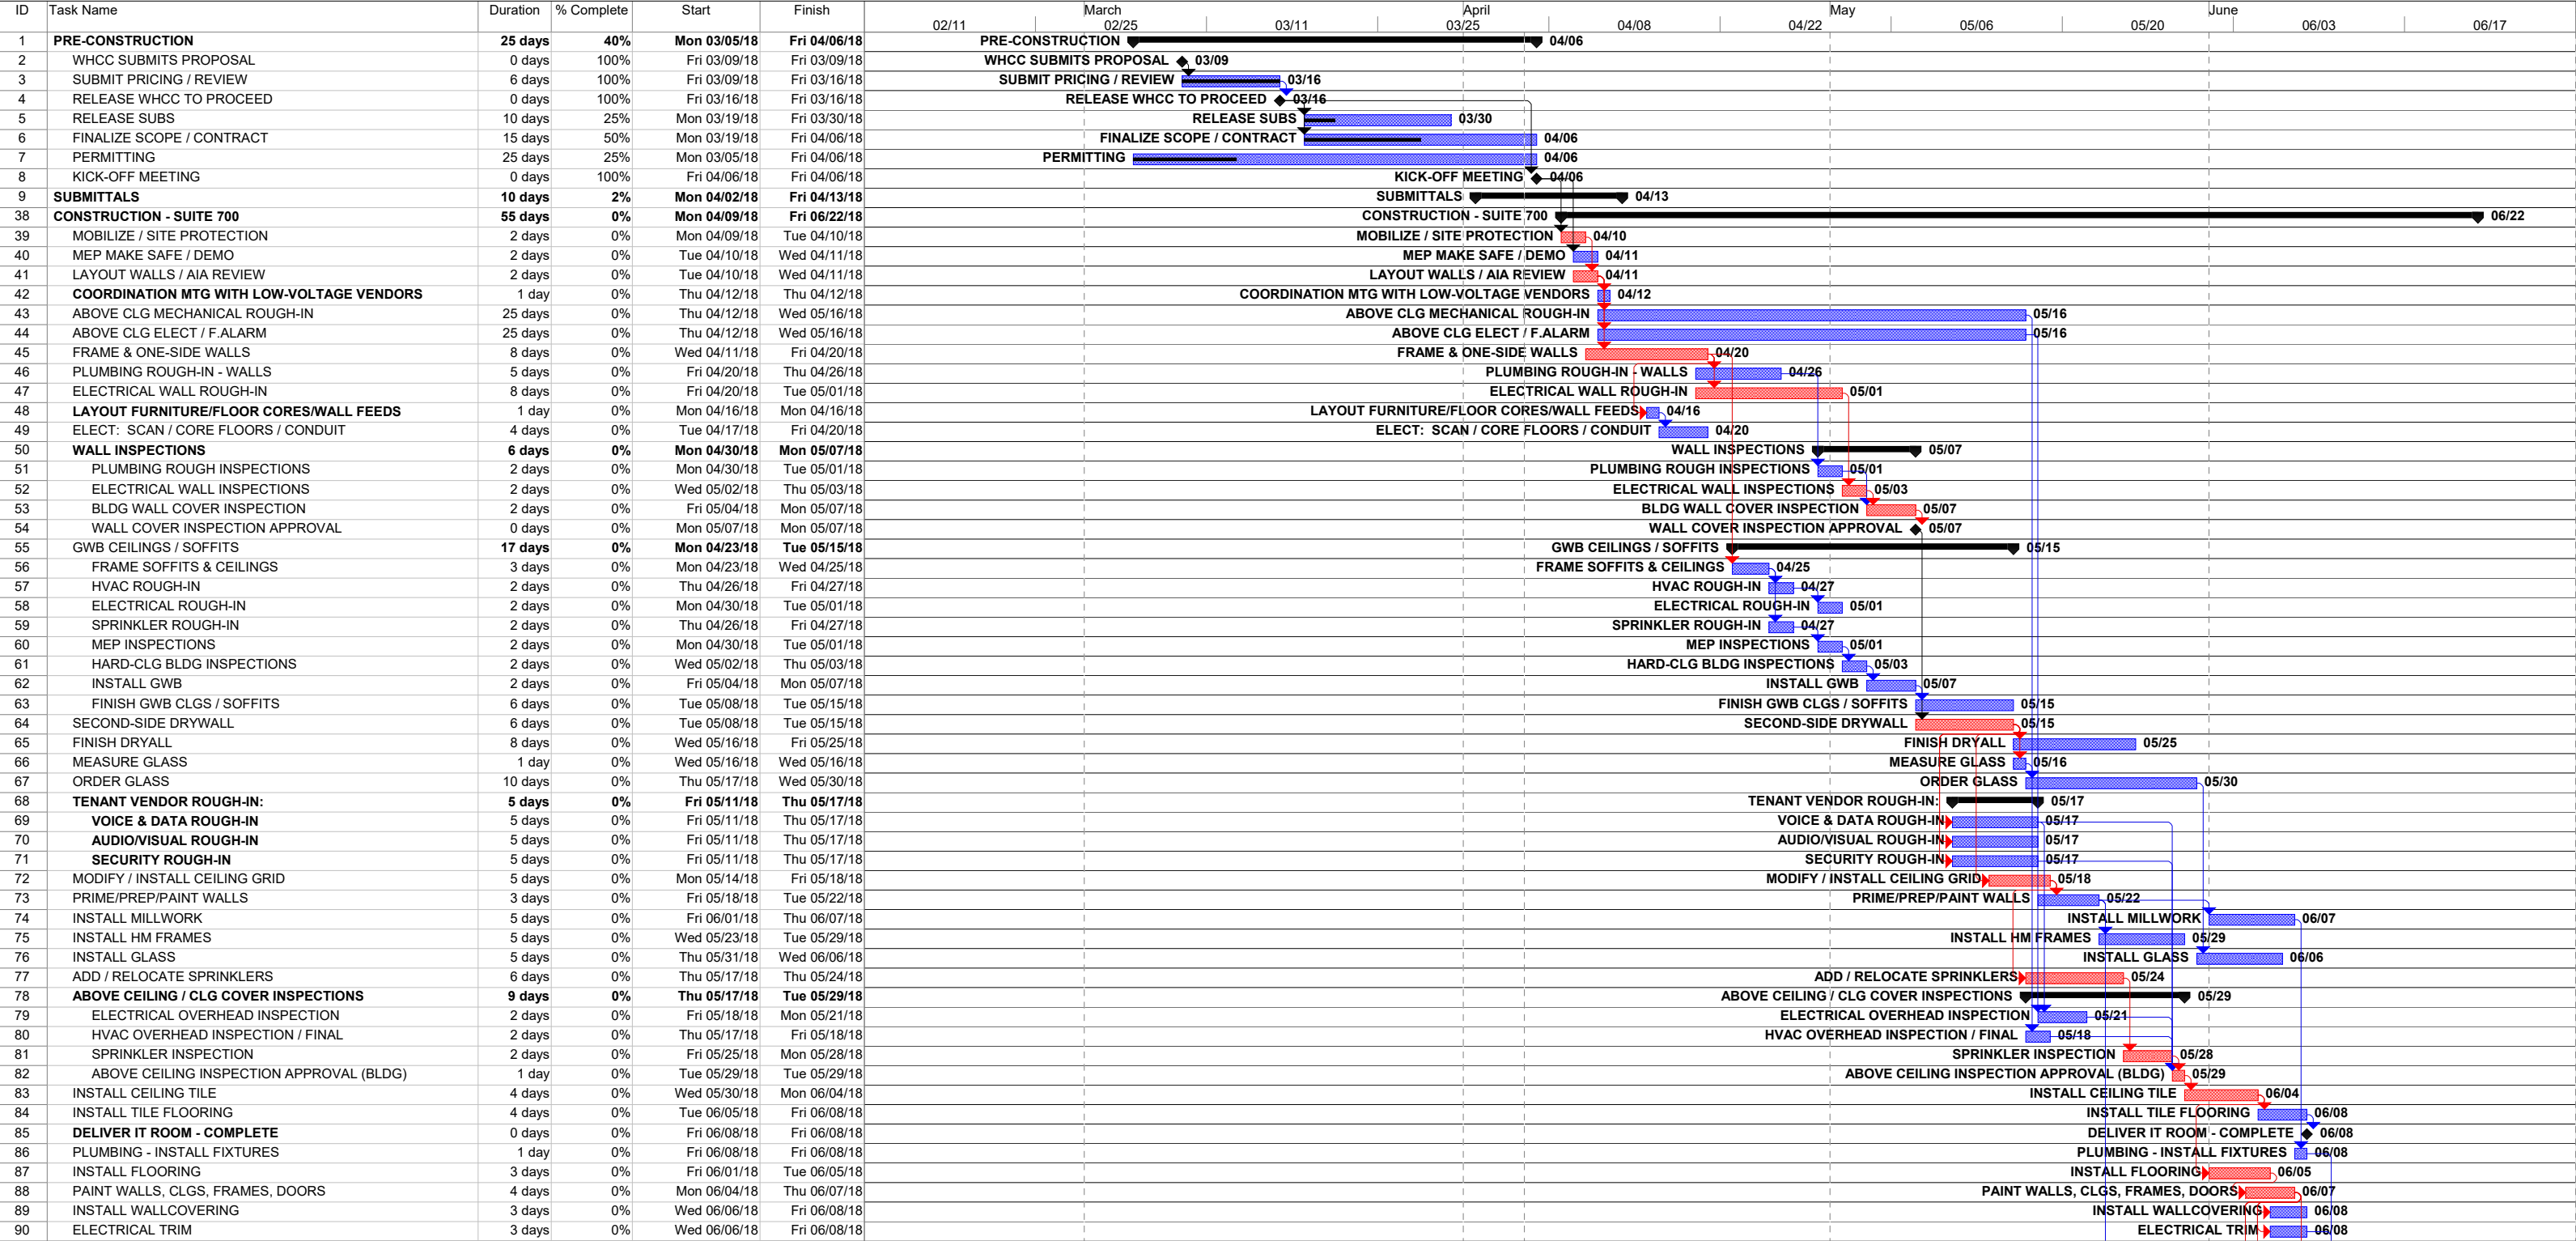

ID	Task Name	Duration	% Complete	Start	Finish	02/11	March 02/25	03/11	April 03/25	04/08	04/22	May	05/06	05/20	June	06/03	06/17
91	INSTALL DOORS & HARDWARE	3 days	0%	Wed 06/06/18	Fri 06/08/18												
92	TENANT VENDOR TRIM / INSTALLATIONS:	3 days	0%	Tue 06/05/18	Thu 06/07/18												
93	VOICE & DATA TRIM / CERTIFICATION	3 days	0%	Tue 06/05/18	Thu 06/07/18												
94	ACCESS CONTROL INSTALLATION	2 days	0%	Tue 06/05/18	Wed 06/06/18												
95	VOICE & DATA TRIM / CERTIFICATION	3 days	0%	Tue 06/05/18	Thu 06/07/18												
96	INSTALL SYSTEMS FURNITURE	17 days	0%	Wed 05/23/18	Thu 06/14/18												
97	DELIVER WHIPS TO THE SITE	1 day	0%	Wed 05/23/18	Wed 05/23/18												
98	INSTALL WHIPS	2 days	0%	Thu 06/07/18	Fri 06/08/18												
99	REVIEW SITE CONDITIONS PRIOR TO FURNITURE INSTALL	1 day	0%	Thu 06/07/18	Thu 06/07/18												
100	DELIVER FURNITURE	1 day	0%	Fri 06/08/18	Fri 06/08/18												
101	INSTALL SYSTEMS FURNITURE	4 days	0%	Mon 06/11/18	Thu 06/14/18												
102	ELECTRICAL / V/DATA CONNECTIONS	3 days	0%	Tue 06/12/18	Thu 06/14/18												
103	TEST & BALANCE	3 days	0%	Mon 06/11/18	Wed 06/13/18												
104	PAINT TOUCH-UP	1 day	0%	Mon 06/11/18	Mon 06/11/18												
105	FINAL CLEANING	2 days	0%	Tue 06/12/18	Wed 06/13/18												
106	FINAL INSPECTIONS	5 days	0%	Mon 06/11/18	Fri 06/15/18												
107	PLUMBING / HVAC FINAL INSPECTIONS	3 days	0%	Mon 06/11/18	Wed 06/13/18												
108	ELECTRICAL / V-DATA FINAL INSPECTIONS	3 days	0%	Mon 06/11/18	Wed 06/13/18												
109	BLDG FINAL / FIRE MARSHALL FINALS--C. OF OCCUP.	2 days	0%	Thu 06/14/18	Fri 06/15/18												
110	TURNOVER TO TENANT	0 days	0%	Fri 06/15/18	Fri 06/15/18												
111	GENERATE PUNCHLIST	1 day	0%	Thu 06/14/18	Thu 06/14/18												
112	COMPLETE PUNCHLIST	6 days	0%	Fri 06/15/18	Fri 06/22/18												



April 5, 2018

